



CTAC Overall Program Evaluation




Percentage of Each Question Meeting Requirements in Last 12 Months

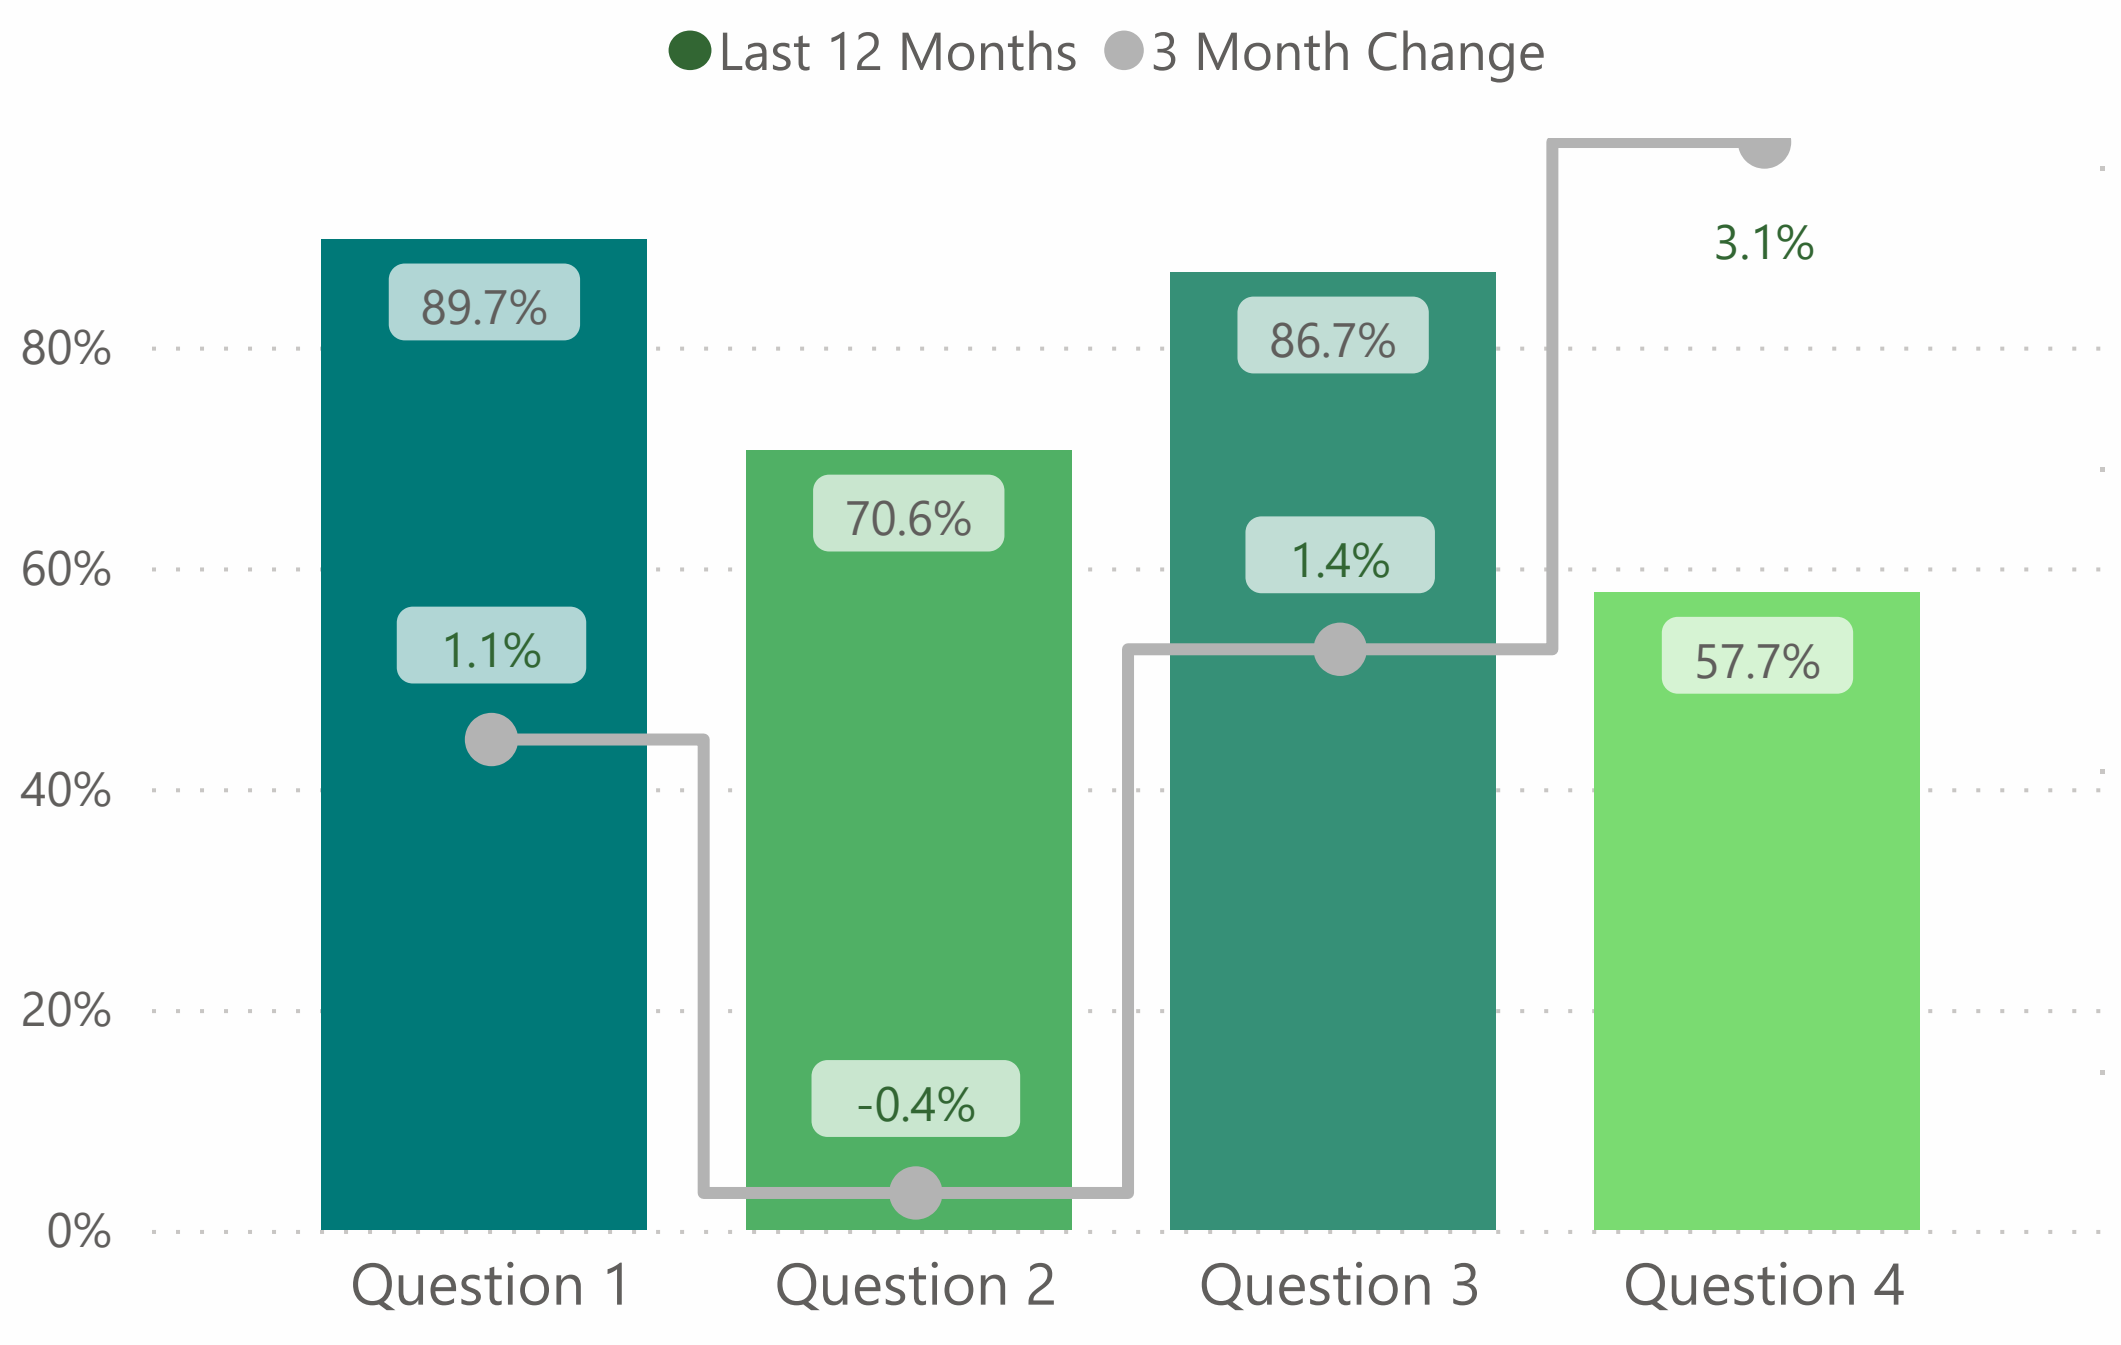

Producer Member Participation

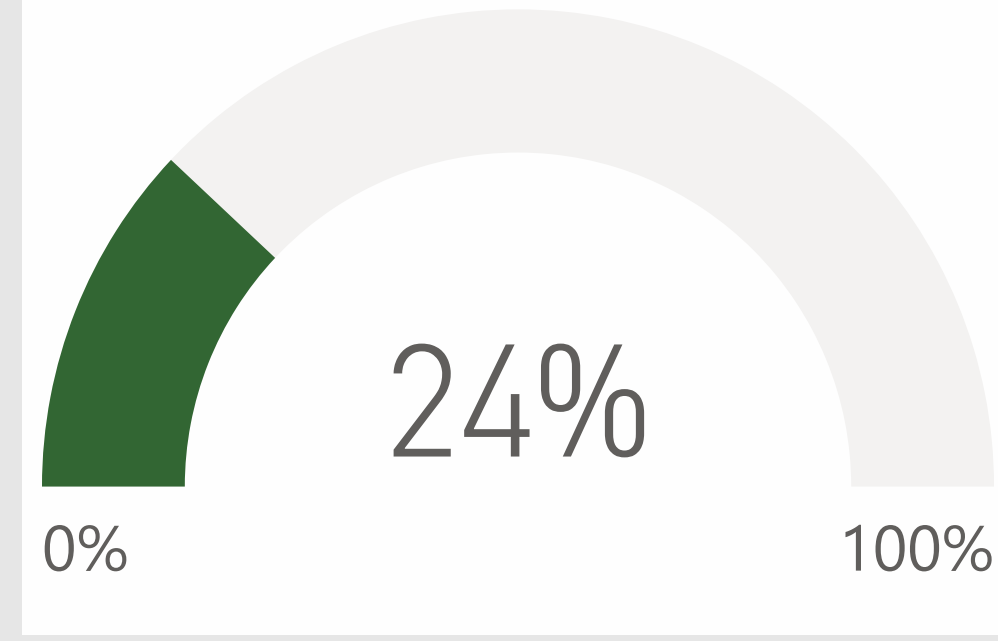


Associate Member Participation

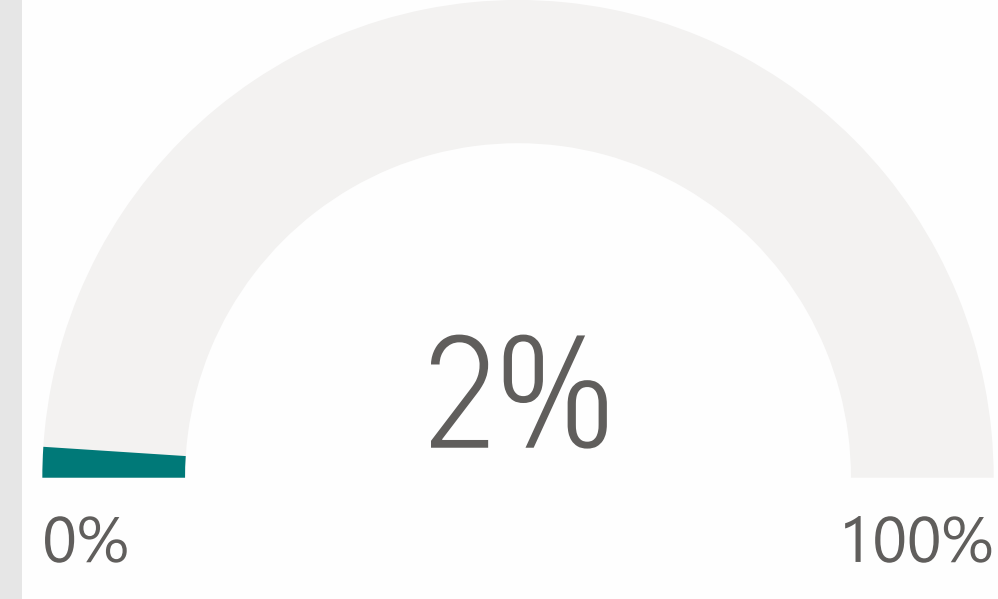

Question	2019	2020	Prev Year Difference
Question 1 Is the testing technician currently ACI Field I certified to test concrete ?	92.0%	89.6%	-2.4%
Question 2 Excluding preliminary check tests, was the concrete sampled in accordance with ASTM C172?	70.1%	70.6%	0.5%
Question 3 Were physical property tests completed and strength specimens molded (if required to cast) in accordance with the appropriate ASTM procedure?	93.1%	86.3%	-6.8%
Question 4 Were the concrete specimens (if required to cast) stored in an initial curing environment following ASTM C31, section 10.1.2, including temperature monitoring?	51.3%	58.1%	6.8%

Observation of Initial Curing Environment

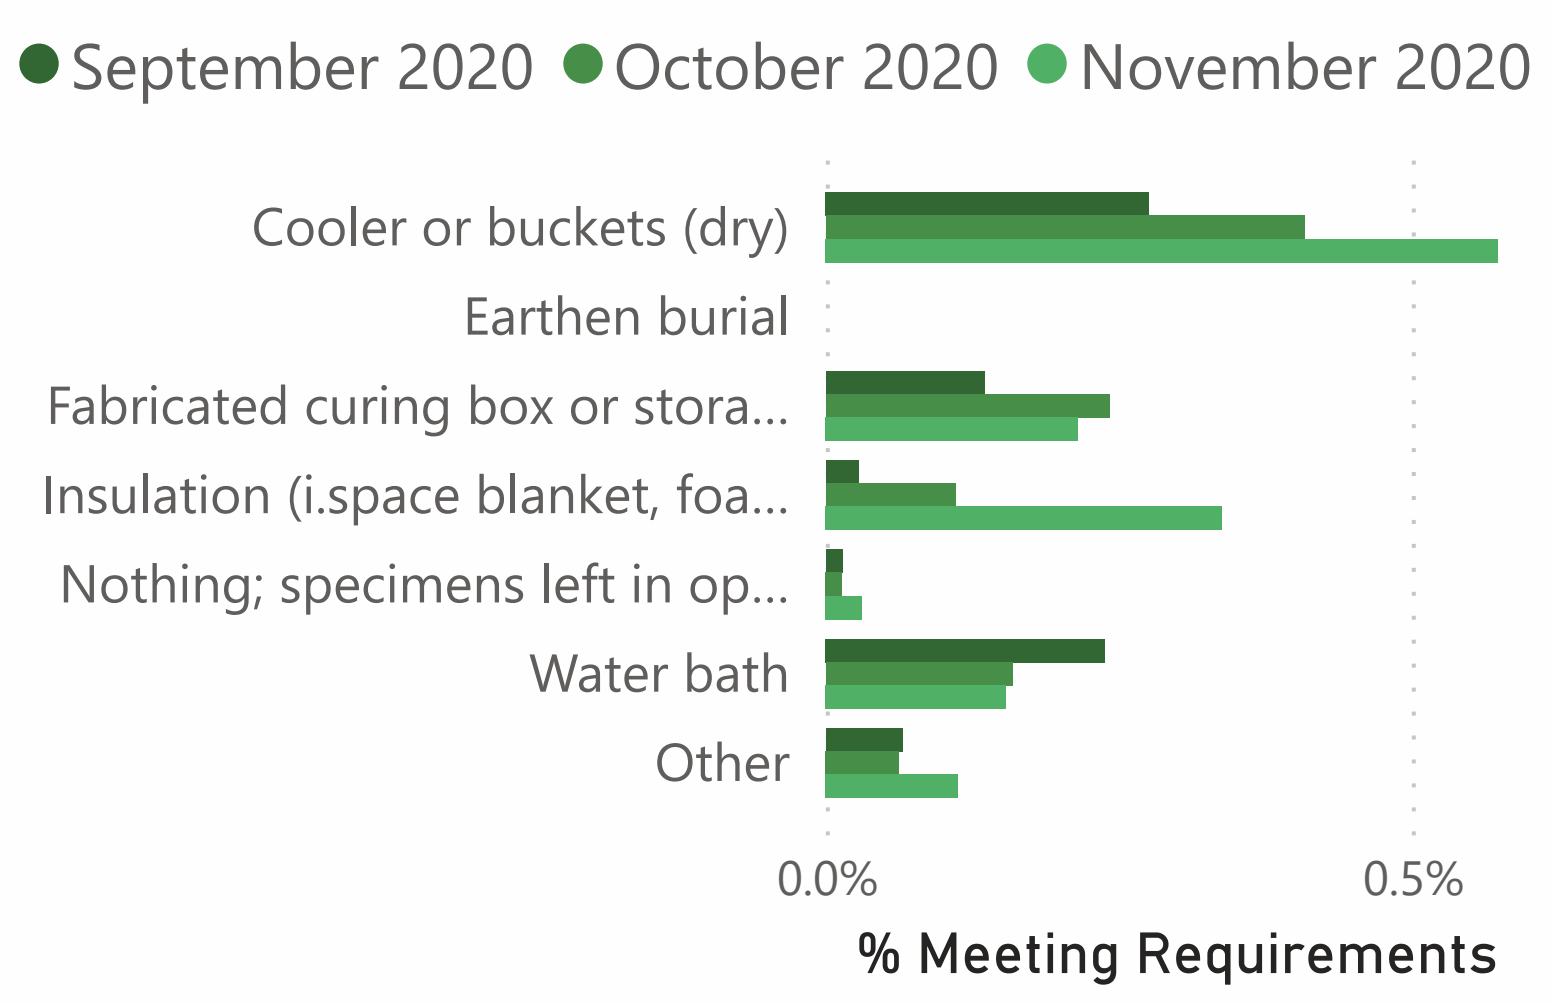

Temperature Monitoring Device Used

