



CTAC Overall Program Evaluation - July 2021




Percentage of Each Question Meeting Requirements in Last 12 Months

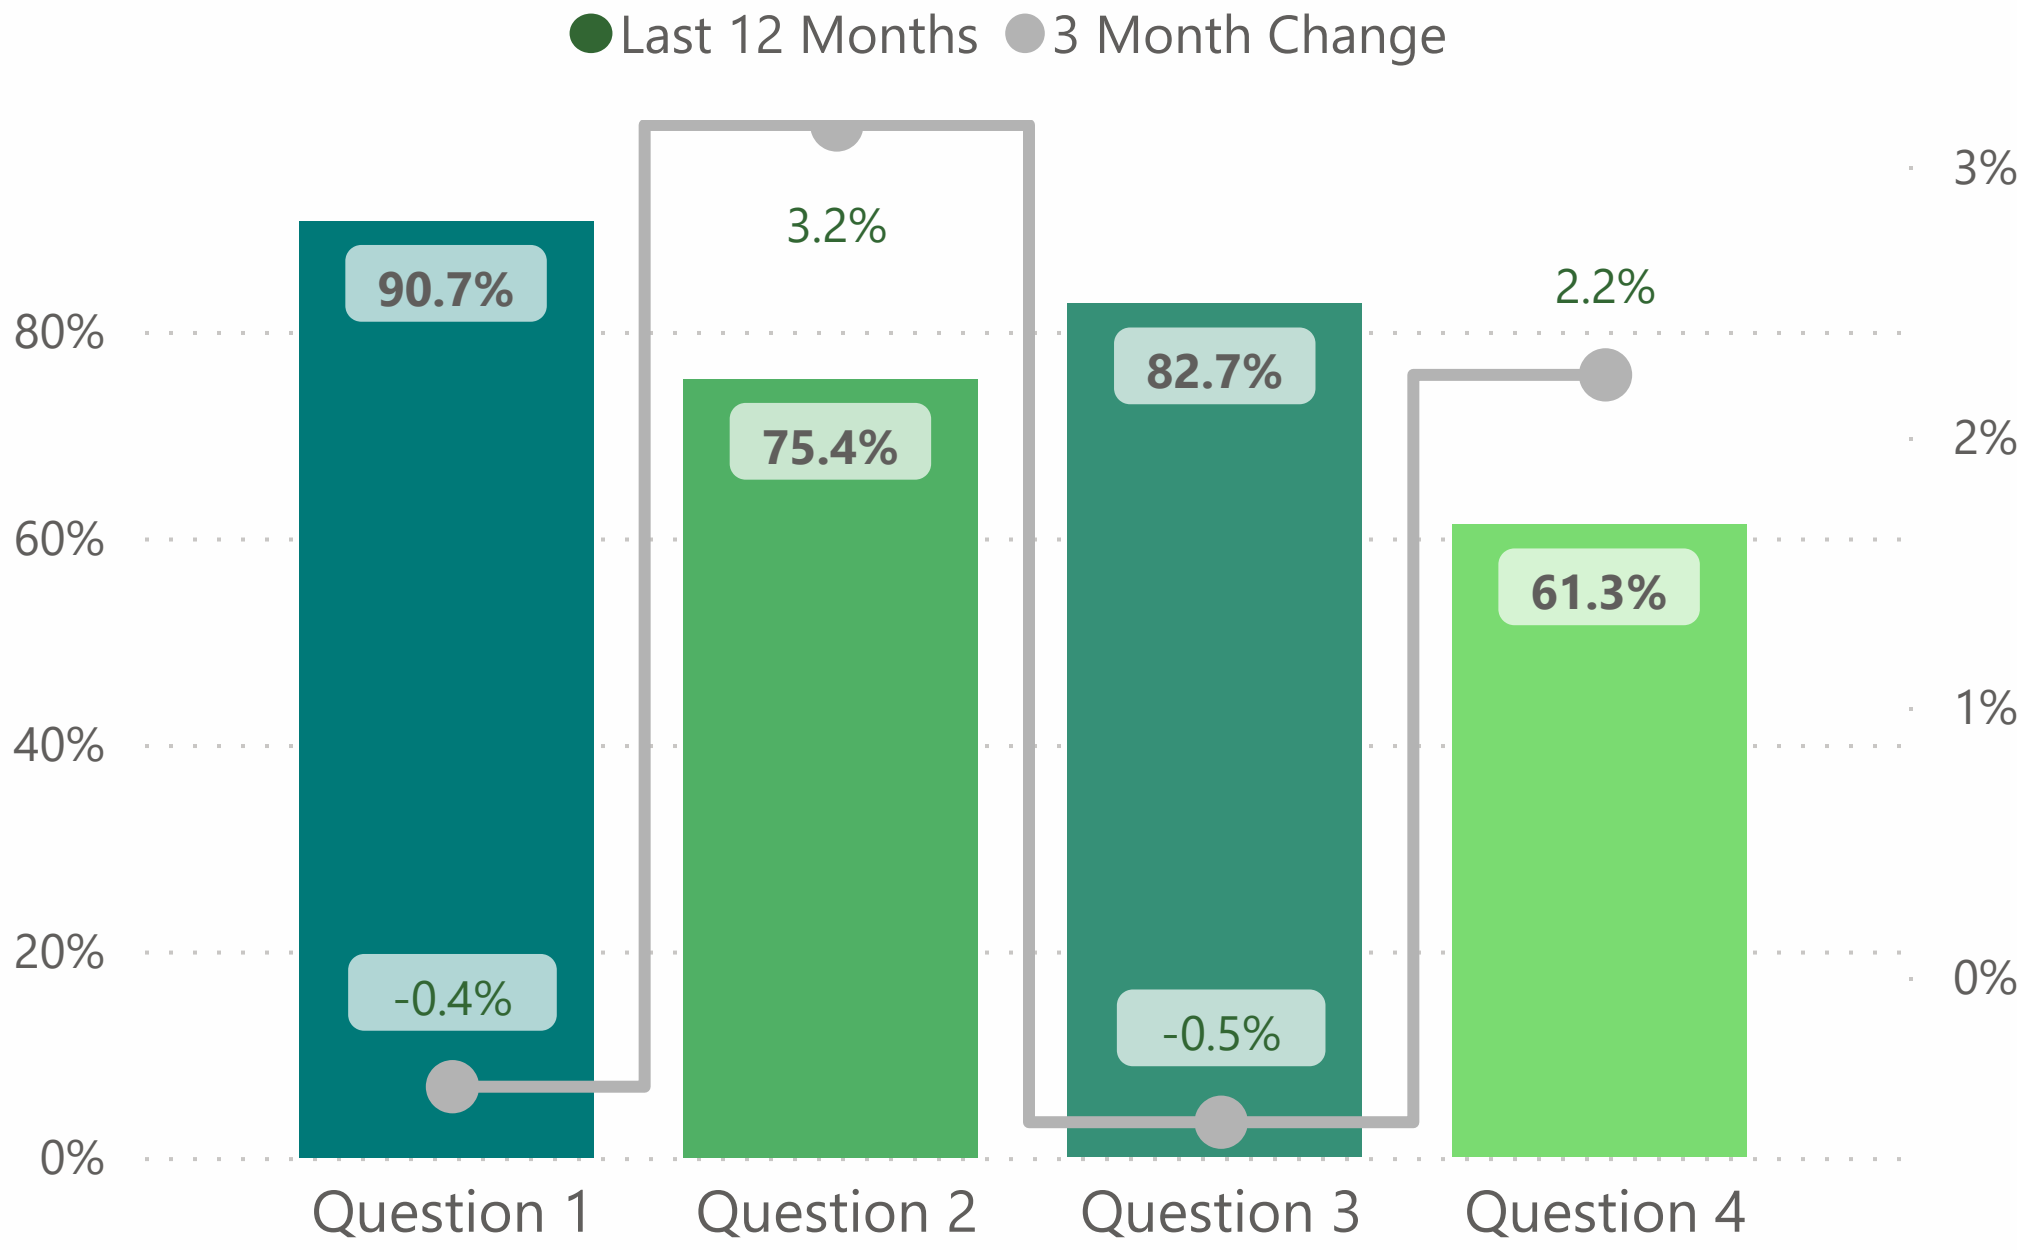

Producer Member Participation

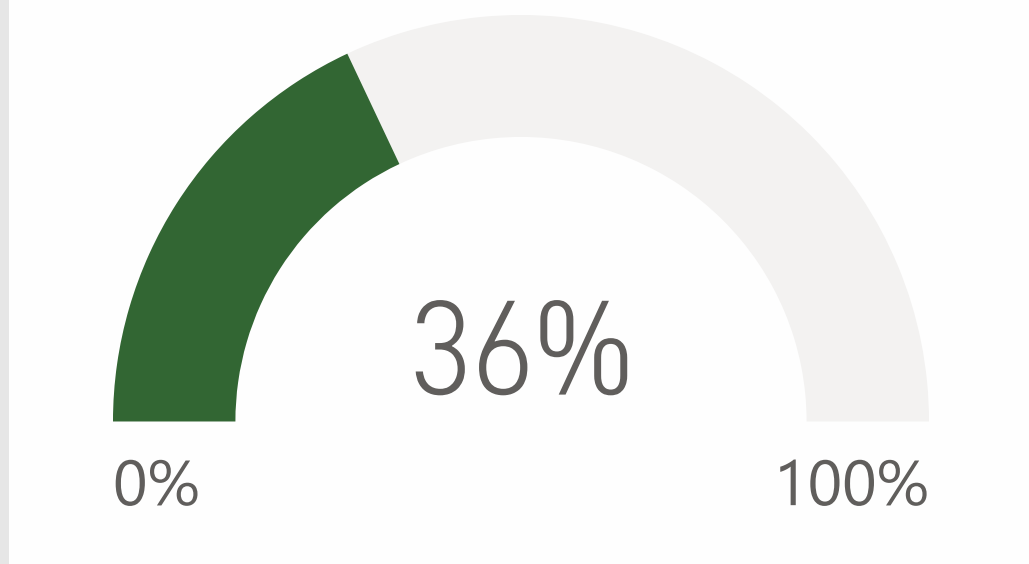


Associate Member Participation

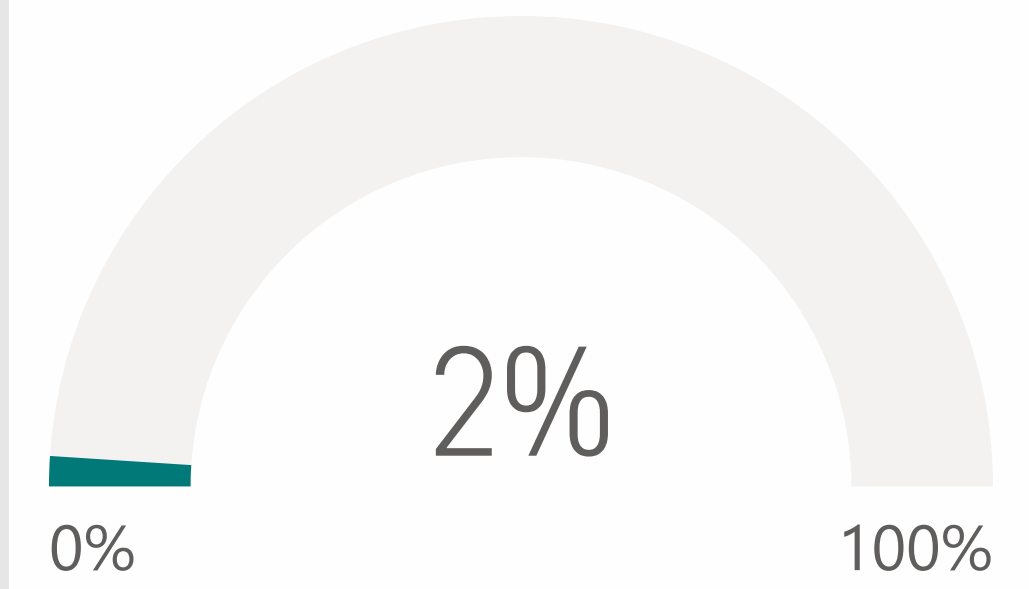

#	Question	2019	2020	2021	Prev Year Difference
Question 1	Is the testing technician currently ACI Field I certified to test concrete ?	91.1%	89.7%	90.0 %	0.3%
Question 2	Excluding preliminary check tests, was the concrete sampled in accordance with ASTM C172?	72.9%	70.1%	77.0 %	7.0%
Question 3	Were physical property tests completed and strength specimens molded (if required to cast) in accordance with the appropriate ASTM procedure?	82.8%	85.8%	80.9 %	-4.9%
Question 4	Were the concrete specimens (if required to cast) stored in an initial curing environment following ASTM C31, section 10.1.2, including temperature monitoring?	48.2%	58.0%	62.0 %	3.9%


Observation of Field Concrete Testing Procedures

● May 2021 ● Jun 2021 ● Jul 2021

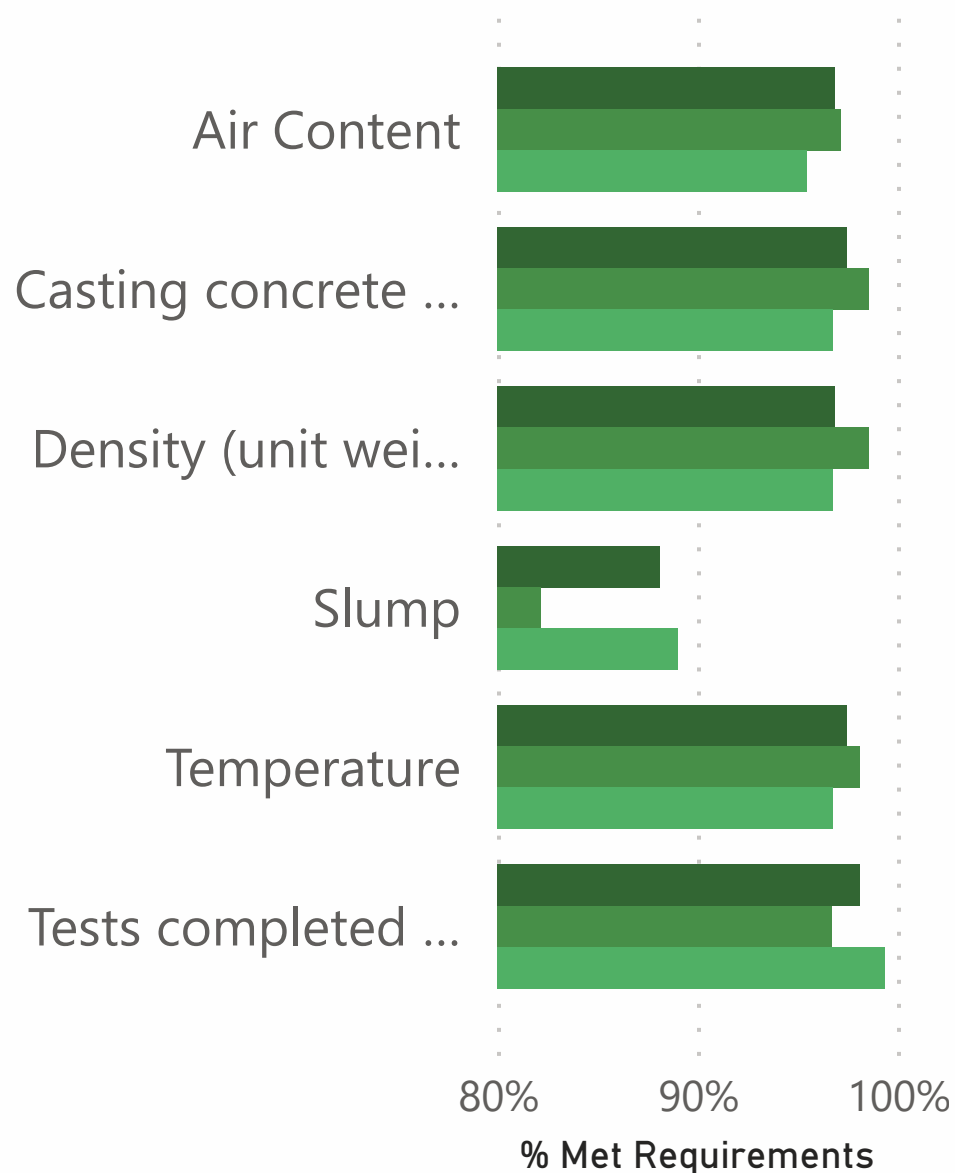

Temperature Monitoring Device Used

● May 2021 ● Jun 2021 ● Jul 2021

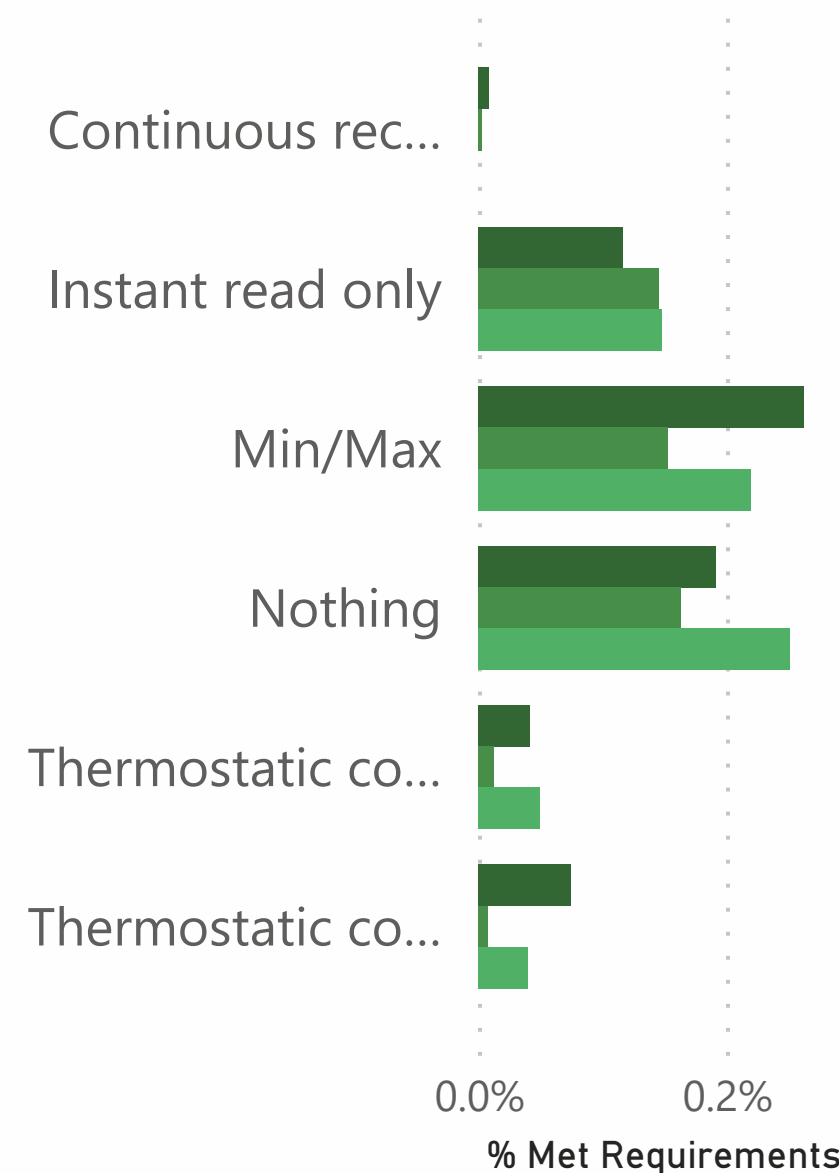

Observation of Initial Curing Environment

● May 2021 ● Jun 2021 ● Jul 2021

